



Mantoloking & Super Storm Sandy

Update #16

Mantoloking & Super Storm Sandy


AGENDA:

- Bay Update
- Debris/Demo
- Replenishment/Easements
- Route 35
- Questions and Answers



Mantoloking & Super Storm Sandy – Bay Update

- Work continues:
 - 70,000 cubic yards to date
 - 130,000 cubic yards to go
- Estimated completion date:
 - Late Sept. / Early Oct.

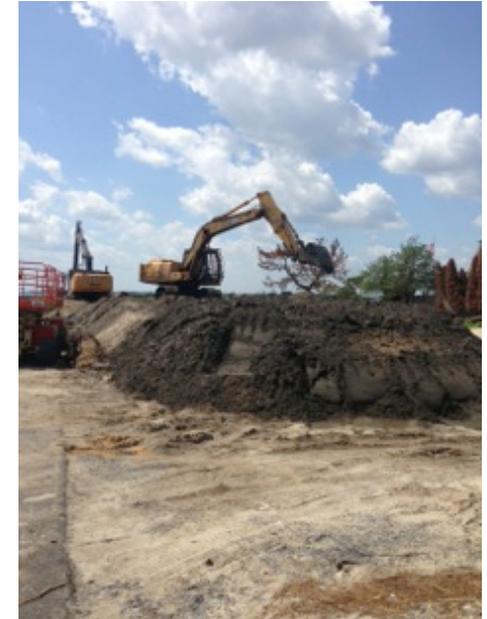

Mantoloking & Super Storm Sandy – Debris/Demo Program – Current Status

- To date– 94 homes in both programs
 - 53 homes demo'd
 - Properties still being cleared



GOAL: Completed by end of this week !!!!


Mantoloking & Super Storm Sandy – Easements / Revetments

- Federal Government *conceptually approved* sheet metal project for Mantoloking and Brick.
 - Needs: plans, permits and easements
 - Cost share: 80% Fed / 20% State
 - Borough installs and maintains sand to cover the steel
 - Hatch Mott working on rock supplement specs

BOTH THE SHEET METAL AND CORPS PROJECT ARE STATE AND FEDERALLY FUNDED– WE HAVE LITTLE CONTROL OR SAY ON TIMELINES

THE STEEL SHEETING IS A SHORT-TERM PROCTIVE MEASURE THAT ACTS AS LAST RESORT- IT COMPLIMENTS THE CORPS PROJECT.

Mantoloking & Super Storm Sandy – Steel Revetment

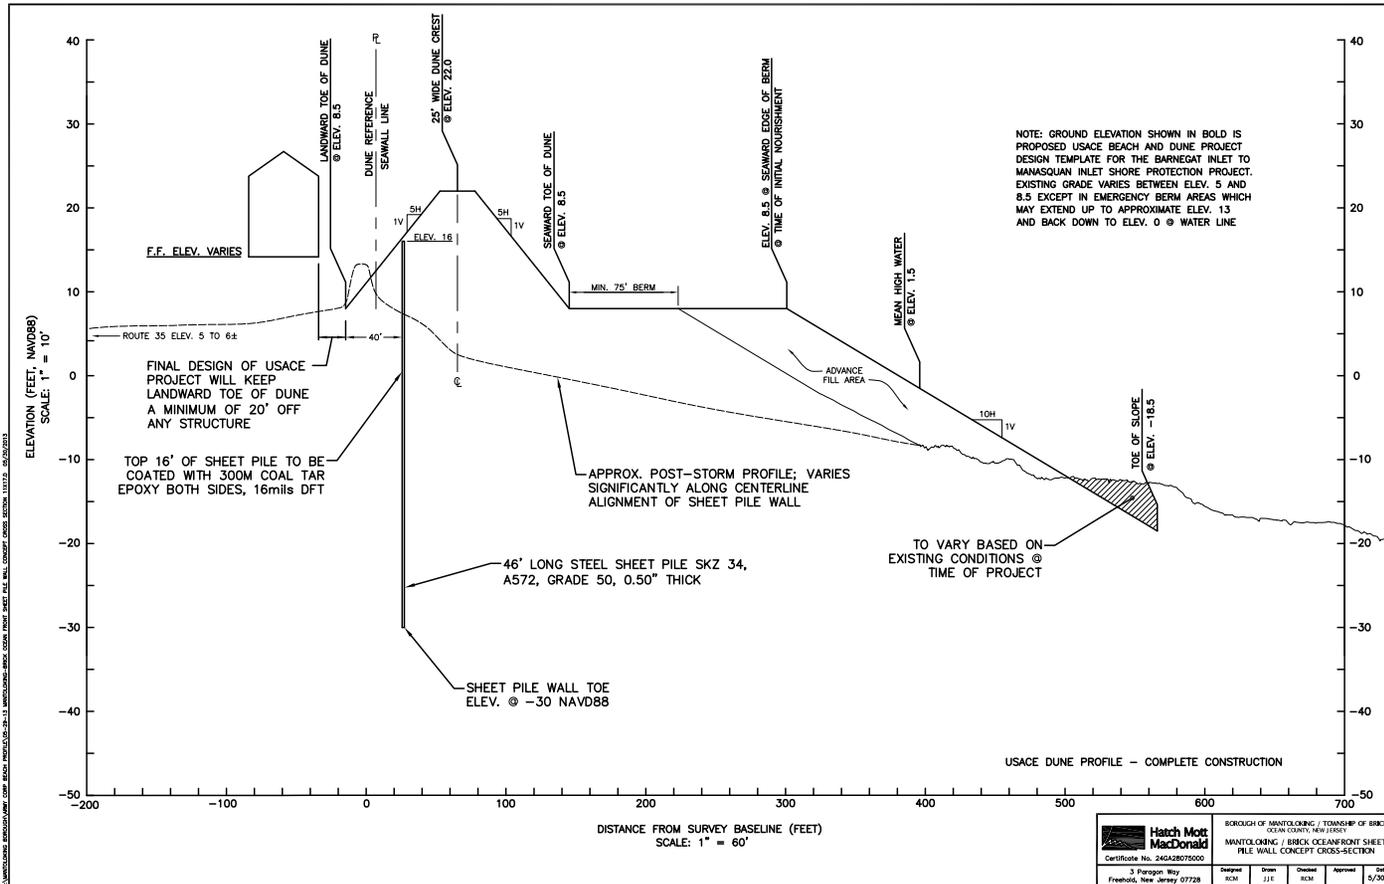

Mantoloking & Super Storm Sandy – Easements / Revetments

MILESTONE	TIMING
Preliminary Sheet Metal design finalized	23 Aug
All revetment easements/USACE easements recorded with Ocean County Clerk	23 Aug
Special TC Meeting held on Aug 28 th to finalize Boro items needed for project.	28 Aug
All project specs submitted to Stakeholders for approval	6 Sept
Bid Specifications are agreed on and ready to go.	6 Sept
Stakeholder Approval granted	20 Sept
Contract for Mantoloking portion goes out to bid (30 day window)	23 Sept
Contract awarded	23 October
First Sheet Driven	29 October



Mantoloking & Super Storm Sandy – Continuous Pressure


Sheet metal completion: Late Fall or Winter

- Emergency protection in place to fill potential gaps
- Need support of State.




Mantoloking & Super Storm Sandy – Route 35

- Gas work ongoing
- Pump Station work to Start on Downer Street next week – Lyman Street- Oct. 1
- Major work starts post Labor day
- Lane closures – Pattern TBD
- Access to Downer/some homes on 35 limited.
- Estimated completion: May 2014

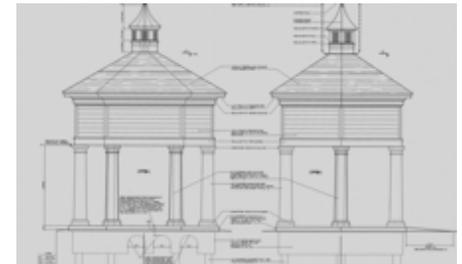

Mantoloking & Super Storm Sandy – Route 35

- Immediate issues to address:
- Pump Station
- Access for Sheet Metal Project

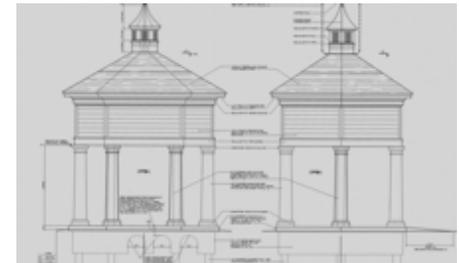

Commissioner Simpson
New Jersey Department Transportation
P.O. Box 600
Trenton, NJ 08625-0600

August 20, 2013

Dear Commissioner Simpson:

I do hope that this letter finds you well. We are excited for the Route 35 project to get underway, and most importantly, for the Sheet Metal project to start so that our community, Route 35 and the communities that the barrier island stands in front of are protected as well.

In that regard, I have two major concerns that we need your assistance with:

- 1) The NJDOT Contractor (Agate Construction) is set to start the project on the 26th of August and to completely close Downer Street. We ask that this work be delayed until after Labor Day. The reason being is that we still have a number of people using Downer Street to access the beach (It is the only access point for a mile to the North and South) and we see a massive traffic issue with concerning both local and transitory use of Route 35; and
- 2) Agate indicated that while working on Route 35, they will be unable accommodate the cranes and large trucks that will deliver and install the sheet metal. As you can imagine, this is completely unacceptable—that sheet metal needs to be our first priority. We cannot afford to wait. One hurricane or strong Nor'Easter will cause massive problems.

We do hope that you will be able to address both of these issues positively and to provide us with a work-around. We appreciate the DOT's accommodation and look forward to your response.

Best regards,

George Nebel



Mantoloking & Super Storm Sandy – Police Boat

- On water stops in July: **120**
- 1st to respond to boating fatality in Toms River
- “no wake zones” established and enforced
- Increased presence and targeted hours



Mantoloking & Super Storm Sandy

QUESTIONS AND ANSWERS

